THANK YOU FOR JOINING US

- If you would like to update your email with us, please email <u>DESLCM@des.wa.gov</u>
- Please save all questions for the end
- We plan 20 minutes for Q&A
- Thank you!



LEGISLATIVE CAMPUS MODERNIZATION

STAKEHOLDER MEETING #15

December 08, 2022



AGENDA

- LCM 90 Day Look Ahead
- LCM Landscape Peer Review Panel and Capitol Campus Arboretum Feasibility Study
- LCM Global: Legislative Modular Building Informational
- Newhouse Building Replacement Informational
- Pritchard and O'Brien Project Informational

90 DAY LOOK AHEAD

December 2022


- PET meeting December 8, 2022
- LCM Stakeholder meeting #15 December 8, 2022
- SCC meeting December 15, 2022
- Legislative Modular Building "Conditional Use" expected December 15, 2022
- LCM Landscape Peer Review Panel meeting #4 December 19, 2022
- City of Olympia Newhouse building permit submittal December 23, 2022

February 2023

- PET meeting February 9, 2023
- LCM Landscape Peer Review Panel #6 February 14, 2023
- Newhouse building permits expected by mid-February
- LCM Stakeholder Meeting #17 February 23, 2023
- Potential Newhouse construction start date early March 2023
- Pritchard and O'Brien SD complete mid-March 2023


January 2023

- 2023 Session January 9, 2023 April 24, 2023
- LCM Landscape Peer Review Panel #5 January 10, 2023
- LCM Stakeholder Meeting #16 January 26, 2023

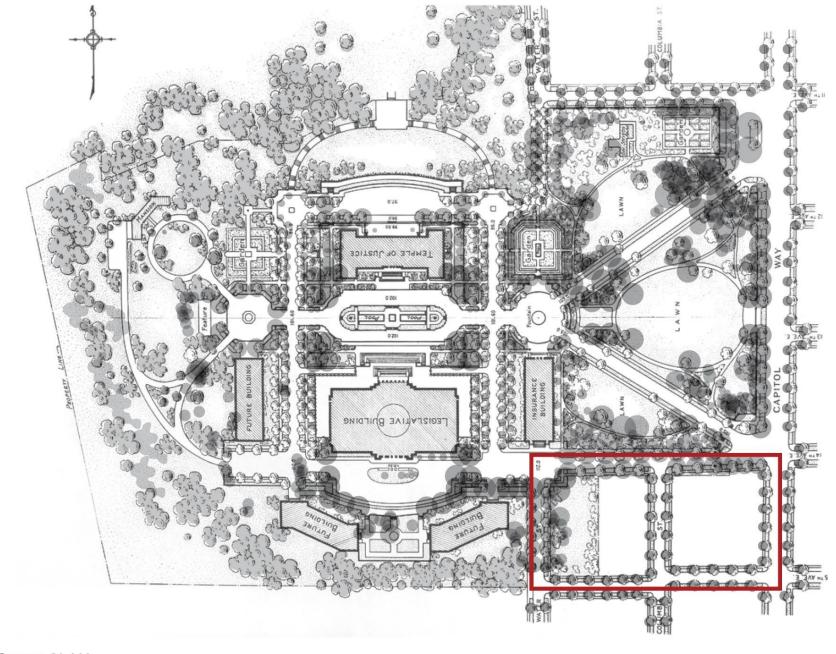





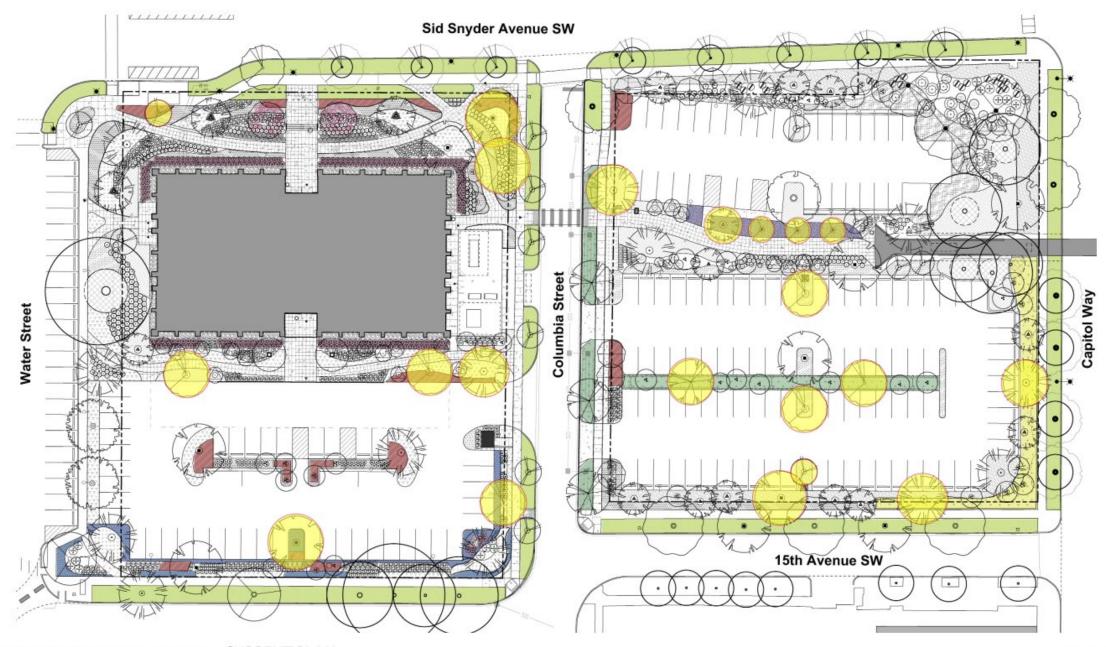





CAPITOL CAMPUS ARBORETUM FEASIBILITY STUDY



WHAT IS AN ARBORETUM?

An arboretum is an area devoted to specimen plantings of trees and shrubs. Distinct from a forest, nursery, or park, it is in a sense an outdoor museum of trees. It is a place where many varieties of trees are grown for research, educational and ornamental purposes; where trees and shrubs are cultivated for exhibition.

OBJECTIVES

- Increase educational opportunities to further enhance visitors' knowledge, understanding, and appreciation of the campus horticultural collection
- Increase visitors' knowledge of the ecosystem services that plants provide to benefit human well-being
- Increase awareness of the Capitol Campus as a destination for visiting, learning, and enjoyment
- Proposed name: Washington State Capitol Arboretum



LEGISLATIVE MODULAR BUILDING




LEGISLATIVE MODULAR BUILDING

- Scope: Two-story building with 16 modules (15,147 SF). Includes south elevator, stairs, and lobby.
- **Schedule:** All 16 modules have been delivered, crane hoisted, stacked & structurally stitched together installed on foundations completed on November 22nd. Continued Modular overall finishing, HVAC, power, data, lighting/ceiling installation will continue thru mid- December. Furniture move-in scheduled for early December with 'Conditional Occupancy' scheduled for mid-December prior to beginning of Legislative Session in January. Note: Elevator installation & commissioning will continue through December and into January 2023.
- Budget: Legislators approved a budget of \$9.5M in total project costs on March 8, 2022.
 GCCM and subcontractors are coordinating procurement schedule for long-lead items (elevator, HVAC units) with very tight supply chain pressure.

LEGISLATIVE MODULAR BUILDING

- **Scope**: Two-story building with 16 modules (15,147 SF). Includes south elevator, stairs, and lobby.
- **Schedule:** Overall finishing (HVAC, power, data, lighting/ceiling installation) continues. Furniture move-in began Monday, December 5 with 'Conditional Occupancy' scheduled for mid-December. Note: Elevator installation and commissioning will continue through December and into January 2023.
 - Legislative Campus Modernization: Modular Building Construction YouTube
- **Budget**: PET approved a budget of \$9.5M in total project costs on March 8, 2022. GCCM and subcontractors are coordinating procurement schedules for long-lead items (elevator, HVAC units) with very tight supply chain pressure.

DRAFT LEGISLATIVE MODULAR BUILDING SCHEDULE

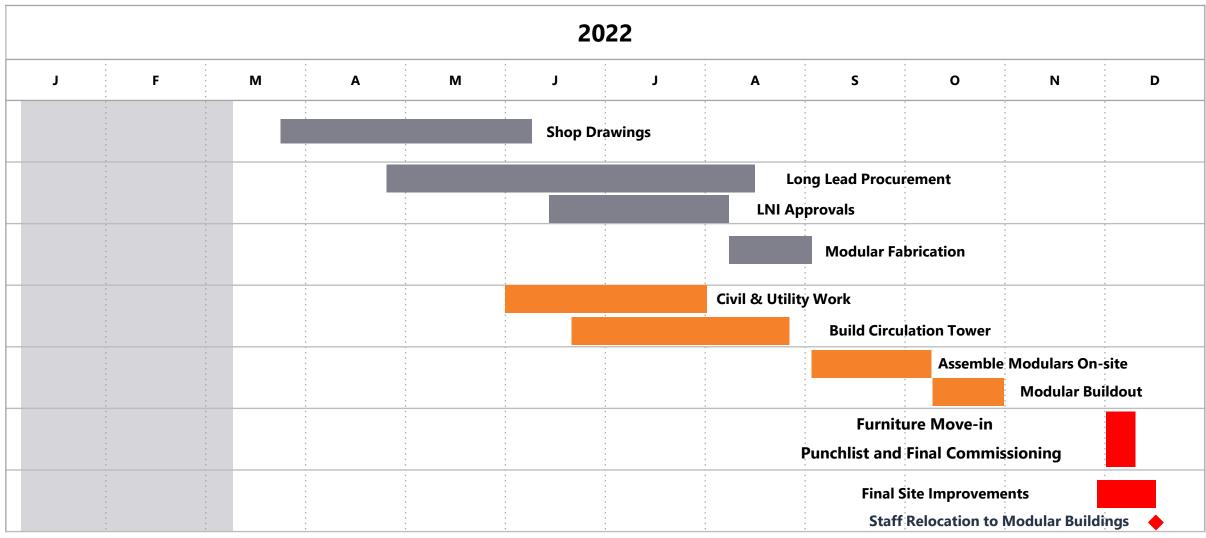

NEWHOUSE BUILDING REPLACEMENT

NEWHOUSE BUILDING REPLACEMENT

• **Scope**: Building provides a total of 59,240 square feet, including an expanded basement for an elevator stop.

Schedule:


- Estimated Substantial Completion date is November 2024.
- o City of Olympia building permit submittal is December 23, 2022.
- Construction Documents (CDs) will be completed on February 27, 2023.

Budget:

- On September 16, 2022, LCM Project Executive Team (PET) approved a budget increase of \$6M for the Newhouse Replacement Building.
- o On October 24, 2022, PET approved a budget increase of an additional \$1.6M.
- Revised total target project cost is \$83.8M (current budget law is \$69M).









Staple Profile - Bronze Frame




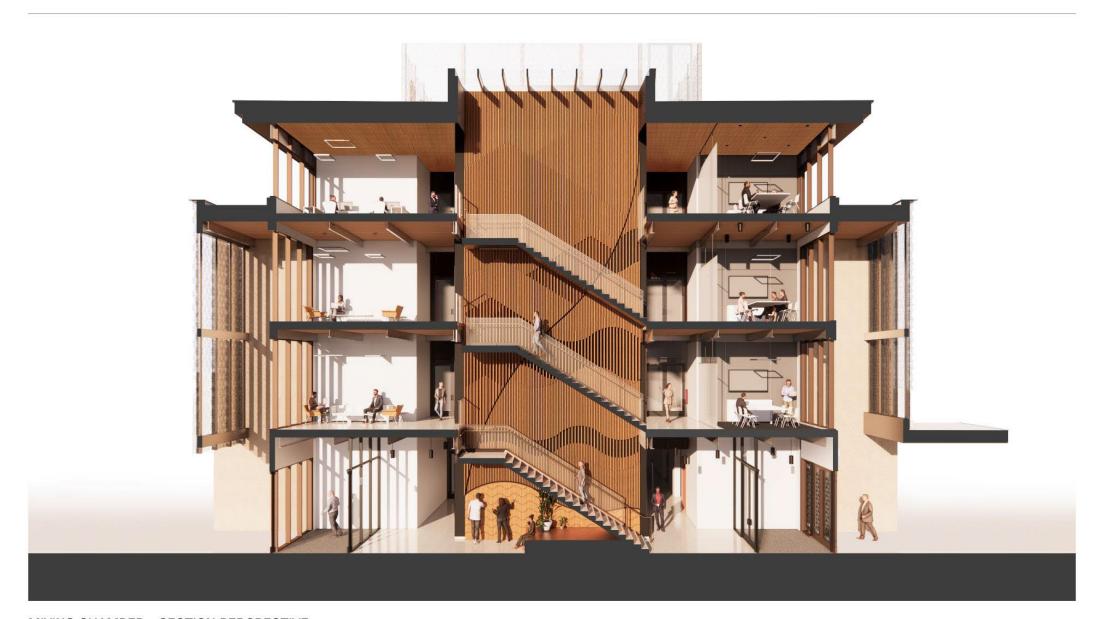

CONSTRUCTION LAY DOWN AND FENCING FEBRUARY 2023 - JUNE 2023

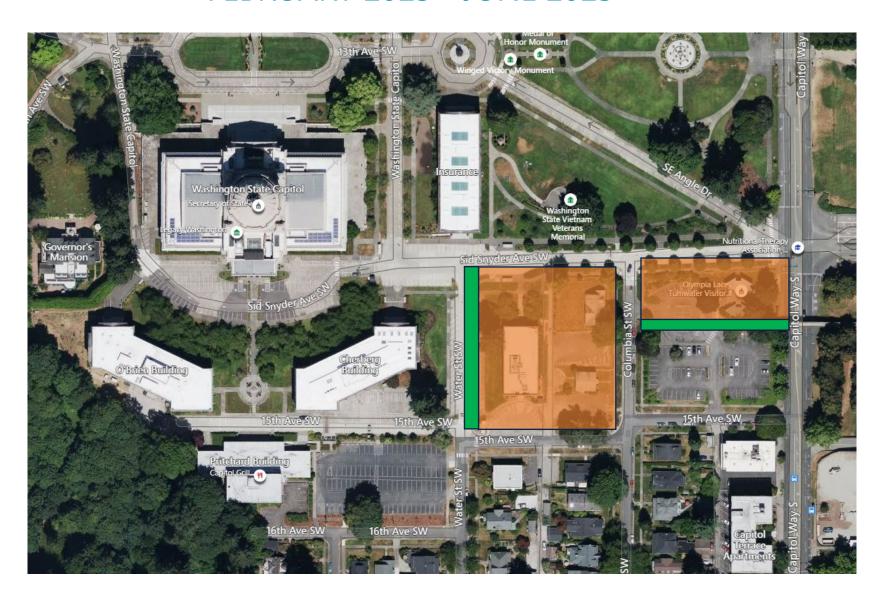

CONSTRUCTION LAY DOWN AND FENCING JUNE 2023 - DECEMBER 2024

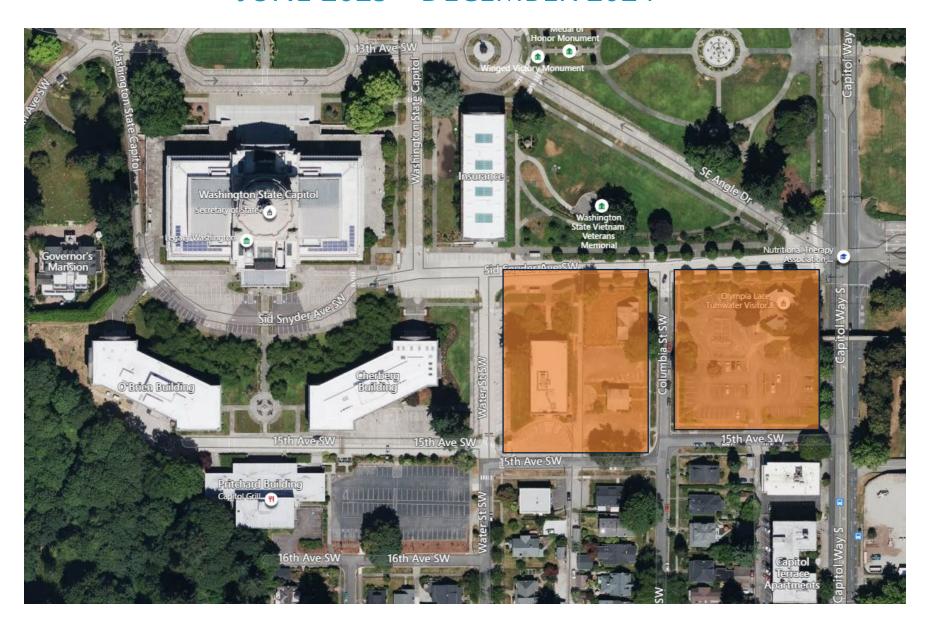


PRITCHARD AND O'BRIEN PROJECT



PRITCHARD AND O'BRIEN PROJECT


- **Scope**: Pritchard Rehabilitation/Expansion is approximately 77,000 SF; O'Brien renovation is approximately 17,630 SF on the third and fourth floors.
- Schedule: Architectural program validation for both buildings is complete. Schematic Design kicked off November 29, 2022.
- Budget: Total target project costs are \$119.4M for Pritchard and \$6.8M for O'Brien.

Pritchard and O'Brien Project Schedule

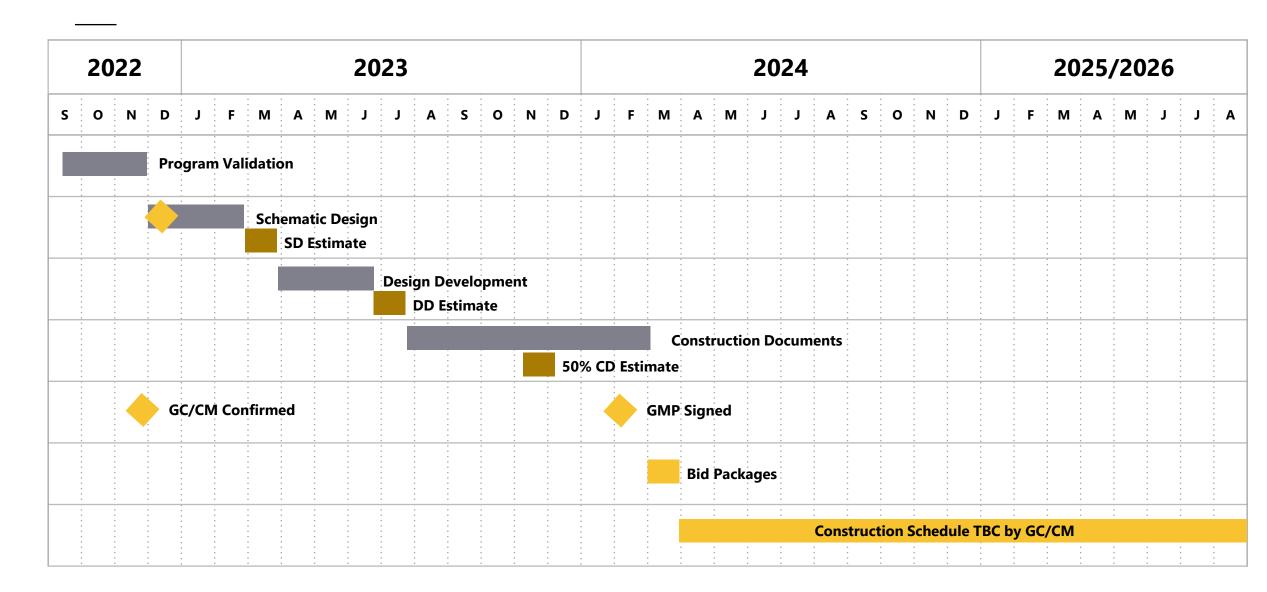






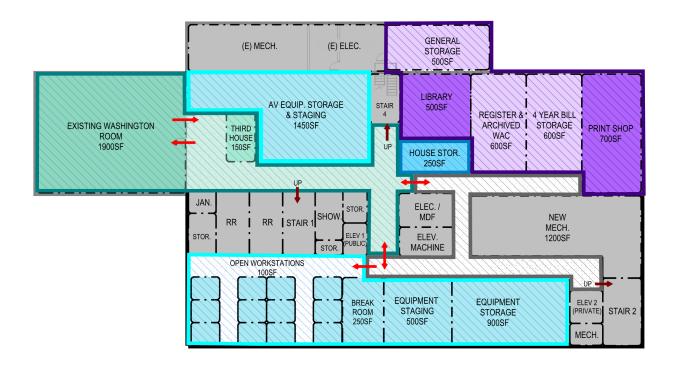


PRITCHARD BUILDING | LEVEL 00 (BASEMENT)






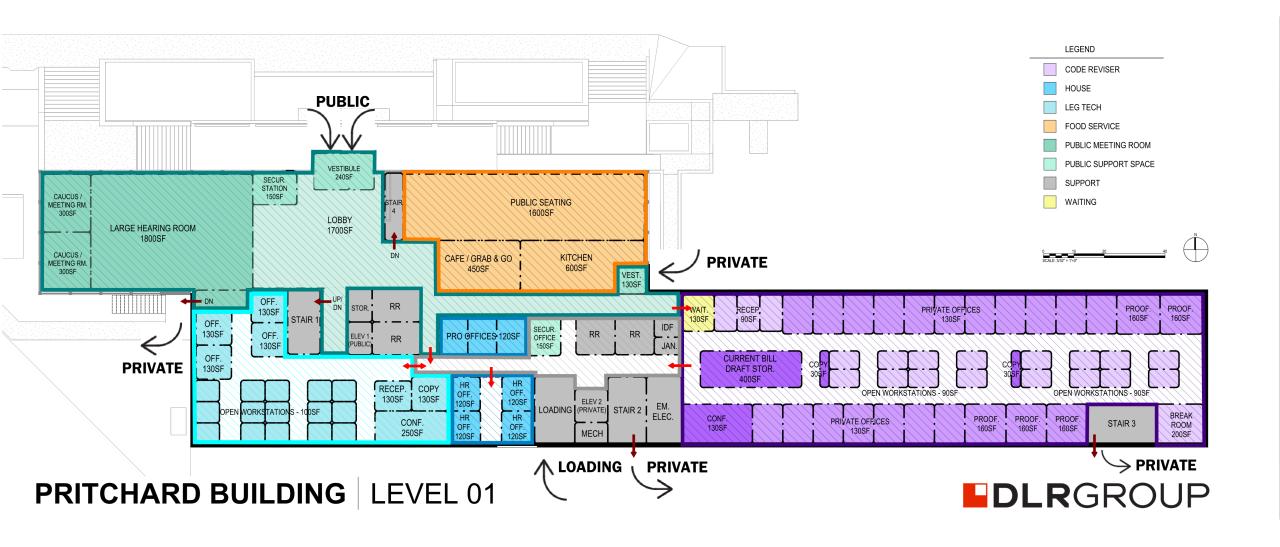

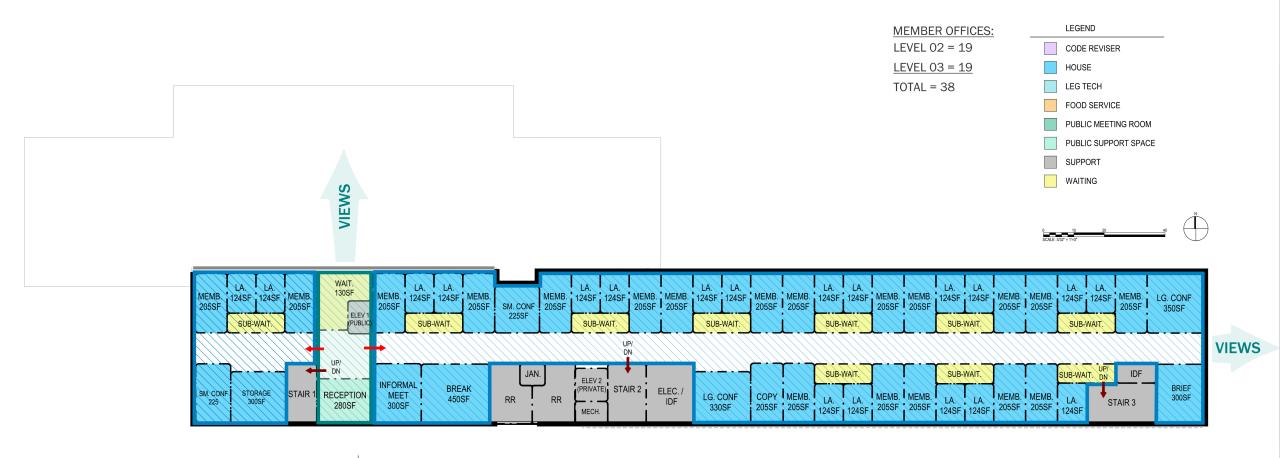

PRITCHARD BUILDING | LEVEL 02



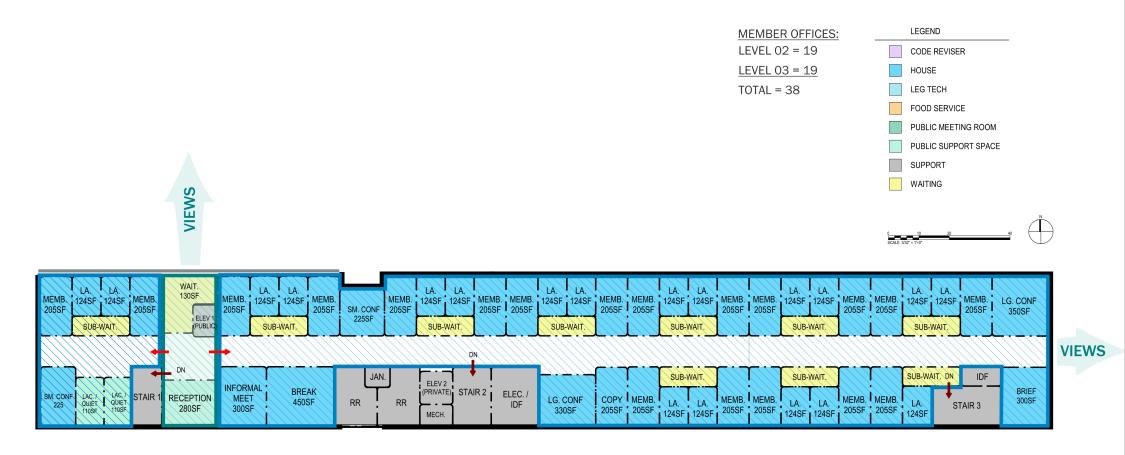


PRITCHARD BUILDING LEVEL 03



Q&A

- Please limit comments to 3 minutes per question/comment
- If there are follow-up questions, please email them to **DESLCM@des.wa.gov**
- All updates regarding stakeholder meeting dates and other LCM updates are posted at <u>Legislative Campus</u> <u>Modernization (LCM) | Department of</u> <u>Enterprise Services (wa.gov)</u> and Public <u>Meeting updates here LCM Public</u> <u>Meetings | Department of Enterprise</u> <u>Services (wa.gov)</u>

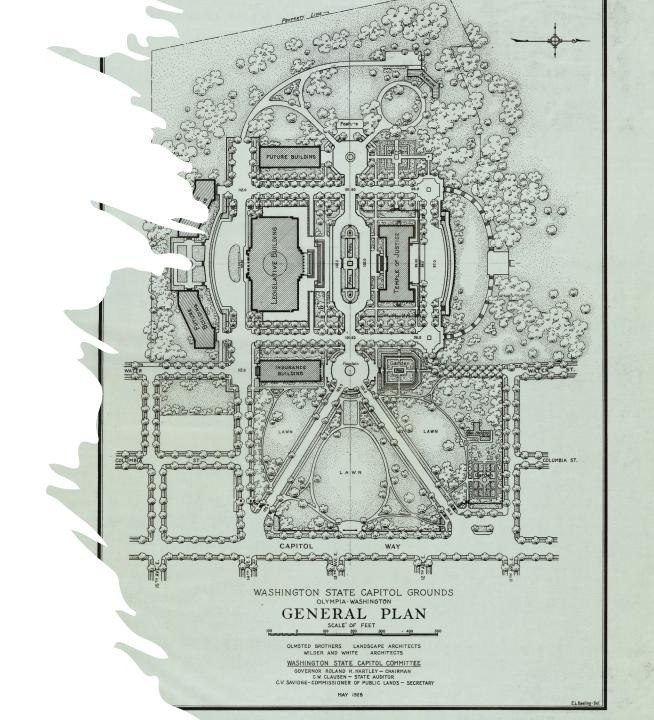

THANK YOU



clarissa.easton@des.wa.gov



360-701-0088



www.des.wa.gov
